




North Terminal Project Overview

February 19, 2015



North Terminal Program Schedule

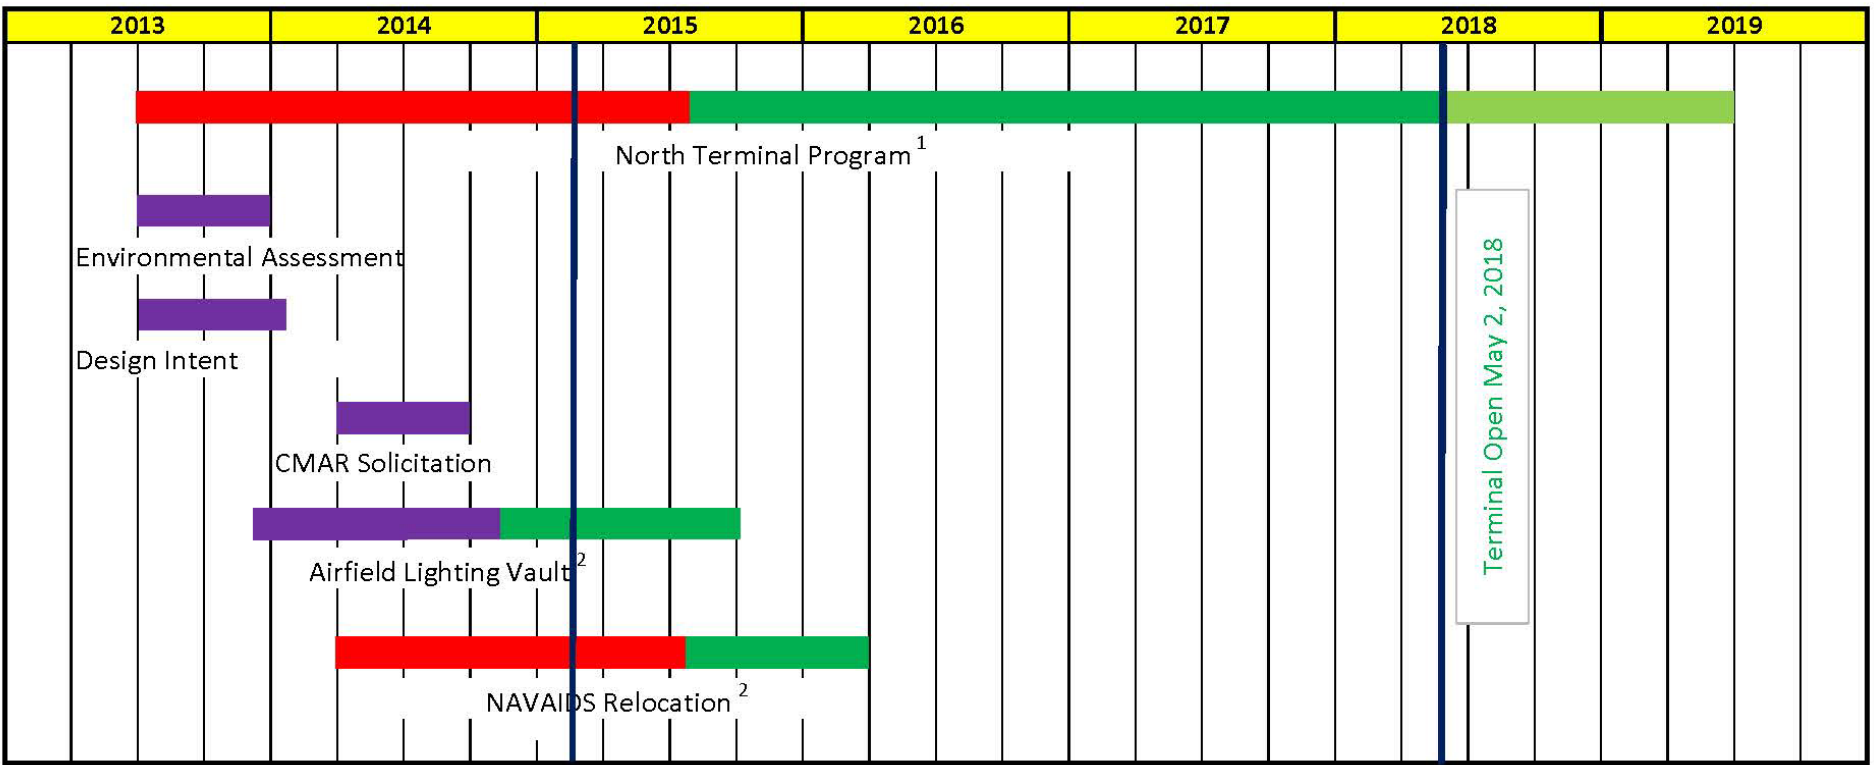

Legend




- 1 Completed by CMAR
- 2 Completed by other parties

Terminal Open May 2, 2018

North Terminal Program

Project Management – DBE Update

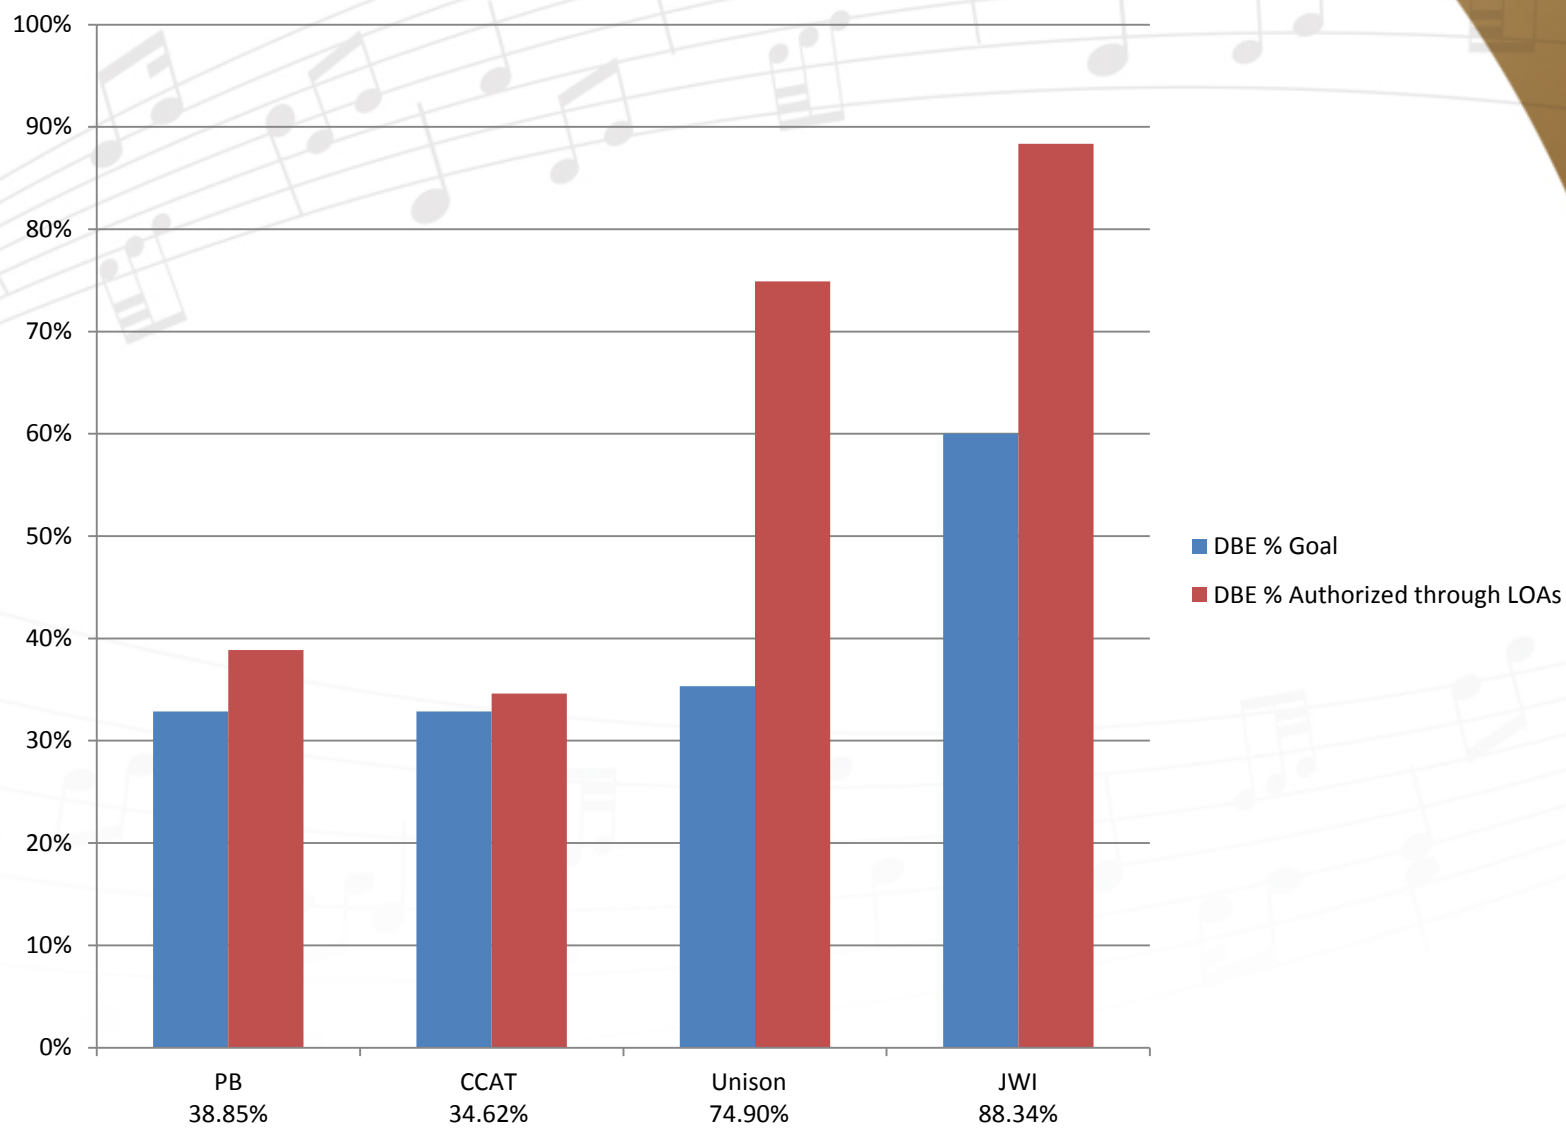

Enabling Projects Status

Project	Status	Completion
Environmental Assessment	Advertised for public comment. Public Meetings Scheduled for November 21 and December 9.	Complete
Supplemental Environmental Assessment	To address changes to the program since the issuance of the FONSI/ROD	July 2015
Kenner Drainage Study	Additional 288 cfs will be combined with drainage improvements required for the North Terminal.	Complete
Site Survey/Subsurface	Final topographical survey documents received.	Complete
CMAR Solicitation	Contract in place Sept 1	Complete
Geotechnical Investigation	Report received June 9	Complete
Airfield Lighting Vault Relocation	Bids Received June 3 Construction began November	Sept 2015
FAA NAVAIDS Relocation	FAA Reimbursable Agreements completed. Design underway.	June 2015

North Terminal Design Status

Project	Status	Completion
Detailed Programming	Completed January 17, 2014.	Complete
Schematic Design	Kick off meeting held January 23, 2014 Completed July 31, 2014	Complete
Design Development	Kick off August 13, 2014 Completed February 6, 2015	Complete
Construction Documents	Kick off February 9, 2015 30% Submittal March 13, 2015 60% Submittal April 17, 2015 95% Submittal May 29, 2015 100% Submittal June 30, 2015	June, 2015



**World Class Airport
for a
World Class City**

Thank You
