



North Terminal Project Update

January 22, 2018

North Terminal Project


Project Components

Project	Status	NTP Date	Completion Date
Pump Station	Operating	Jan, 2016	Dec, 2017 ✓
NAVAIDs – ASR/LLWAS	Complete	Feb, 2016	Dec, 2017 ✓
NAVAIDs – RTR Relocation	Complete	June, 2016	Dec, 2017 ✓
NAVAIDs – Cable Loop	Complete	Jan, 2016	Mar, 2017 ✓
North Terminal	Construction	Jan, 2016	Feb, 2019
Terminal Access Road*	Construction	Dec, 2017	Jan, 2019
Hydrant Fueling*	Construction	Feb, 2017	Feb, 2019

* third party project

North Terminal Program


Project Management – CMAR Invoice Processing Duration

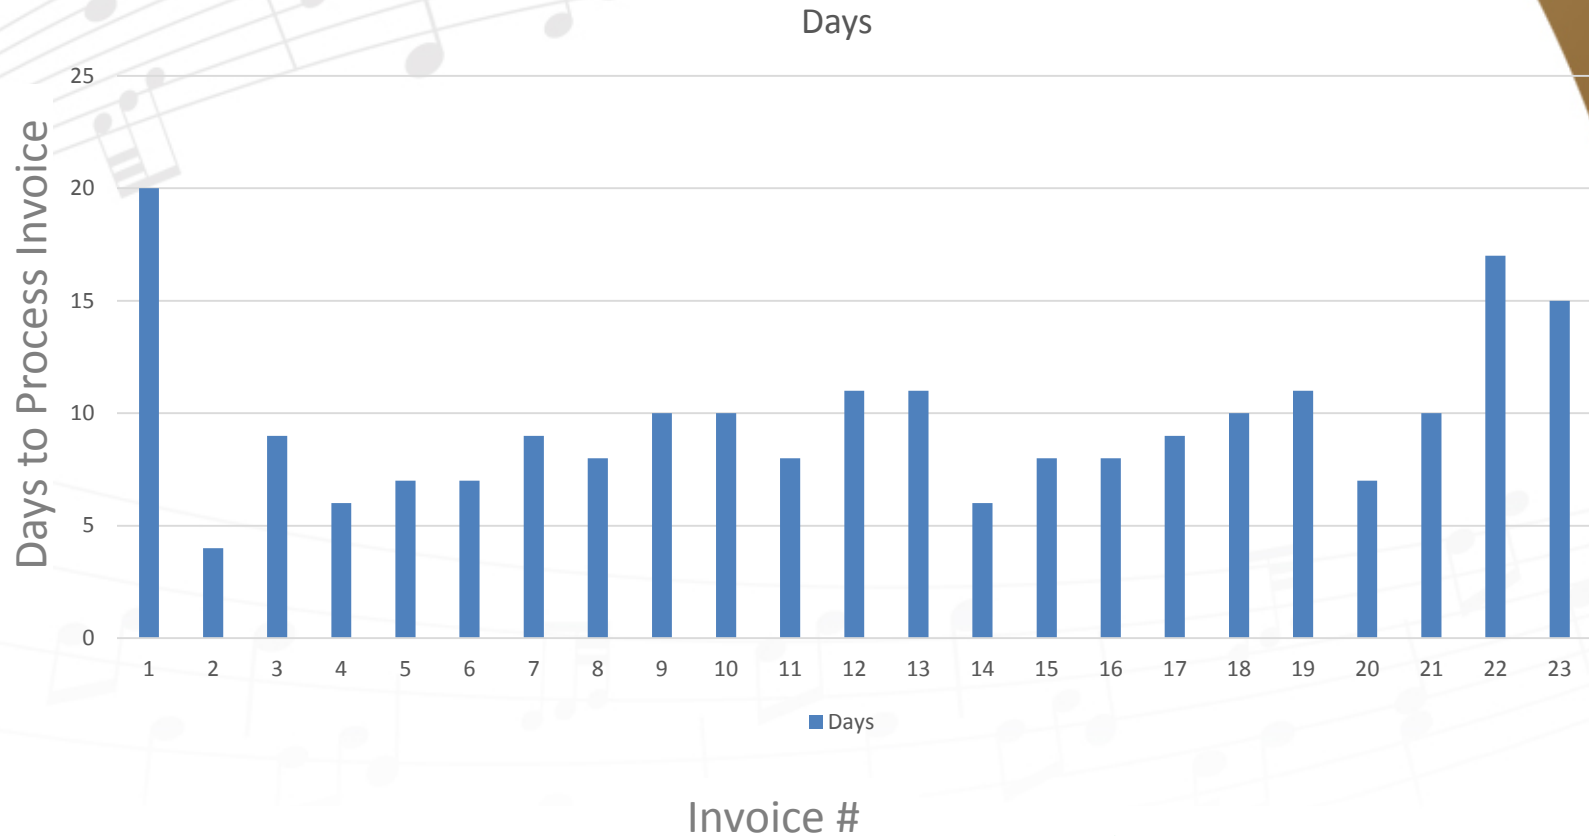

- 20 day process duration requirement met ✓
- 9.6 day average

North Terminal Program

Program Management - Professional Services Invoice Processing Duration

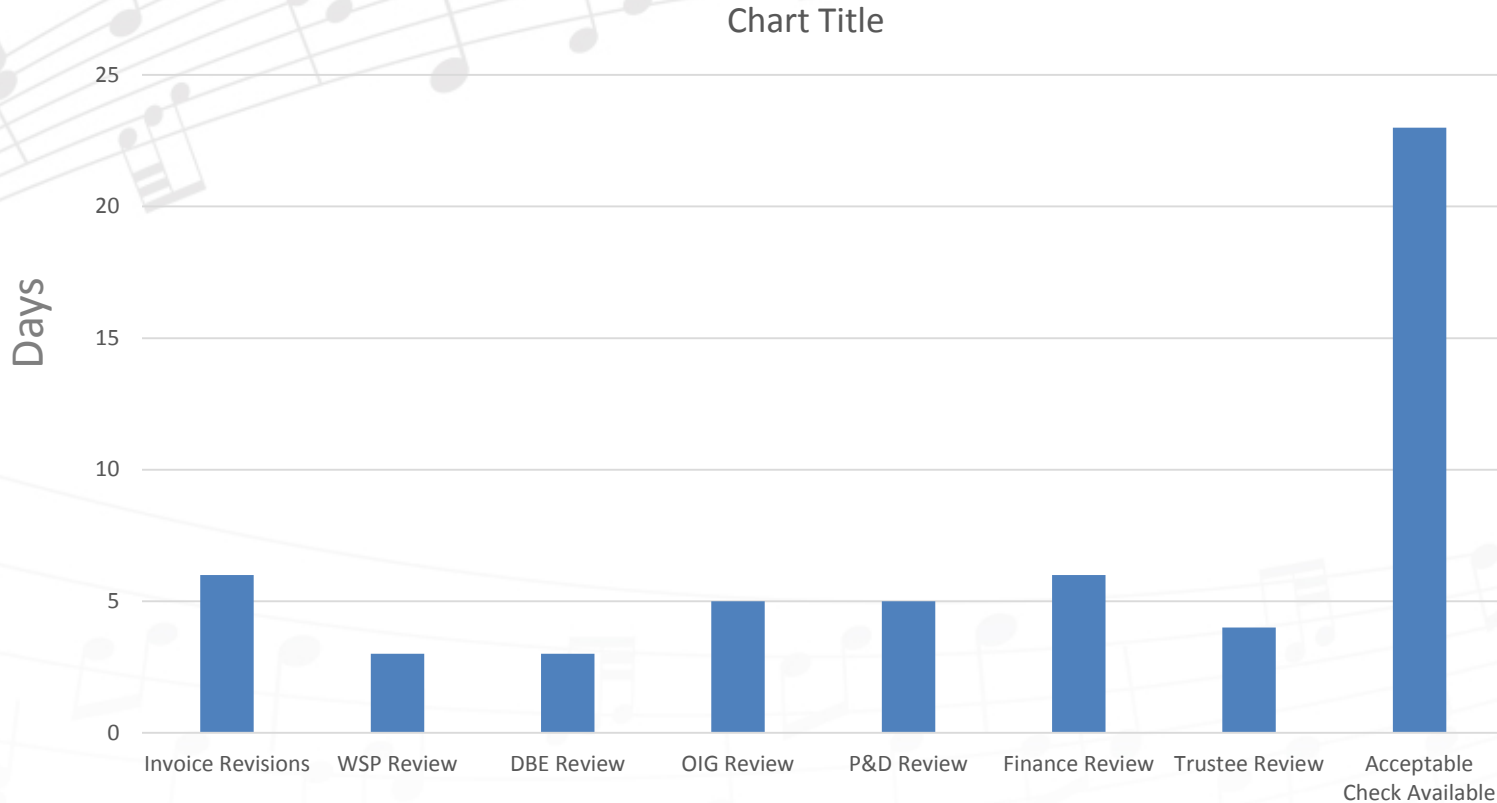

- 23 days to process an invoice
- Goal is to process invoices within 30 days ✓

North Terminal Project

November/December Activities

- North Terminal
 - Schedule
 - Terminal, Concourses B & C
 - Concourse A
 - Civil Work
 - New risk exposure – paving settlement continues
 - Progress – Charlie Pruitt to provide
- Enabling Projects
- Storm Water Pump Station
 - Final Test & Turnover
- NAVAIDs - Complete

North Terminal Project

Aerial January 3, 2018

CMAR Construction Activities



North Terminal Project CMAR Construction Activities





**World Class Airport
for a
World Class City**
